

Burn-Down Chart — Sprint 2

Team: Bruce Schulz, Zach Kahler, Nova Denton-Parry, Jeremy Kirkpatrick

Course: CIS248 Advanced App Development
Summer 2026 — **Deliverable 3**

Sprint Overview


Parameter	Value
Duration	3 weeks (15 days)
Total Points	46
Team Size	4
Target Velocity	~15.3 pts/week

Daily Burn-Down Data

Day	Ideal	Actual	Notes
0	46	46	Sprint 2 begins
1	42.9	45	Wardrobe add wiring (US-03)
2	39.9	43	US-03 complete (Nova)
3	36.8	41	US-04 filter UI done (Nova)
4	33.7	38	US-06 save path wired (Jeremy)

5	30.7	35	US-06, US-07 done (Jeremy)
6	27.6	32	US-17 edit/deactivate (Nova)
7	24.5	29	US-08 suggestions begins (Bruce)
8	21.5	26	US-09 history wiring (Zach)
9	18.4	23	US-10 notifications (Zach)
10	15.3	21	US-13 auth guard (Bruce)
11	12.3	19	US-16 image widget (Jeremy)
12	9.2	17	Continued wiring
13	6.1	15	Bug fixes, state mgmt
14	3.1	14	Integration testing
15	0	13	Sprint ends — ongoing

Burn-Down Chart

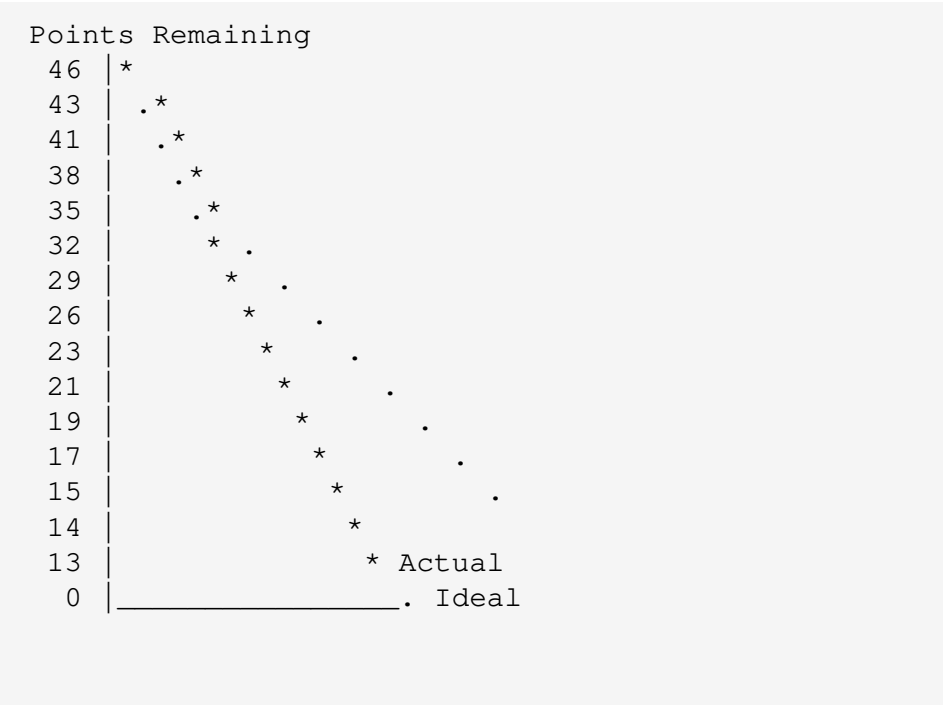

|---|---|---|---|---|
D0 D3 D6 D9 D12 D15

* = Actual . = Ideal

Velocity Analysis

Metric	Value
Planned	46 pts
Completed	33 pts
Remaining	13 pts
Completion	72%
Velocity	~11 pts/week
Sprint 1 Velocity	~24.3 pts/week
Combined Avg	~17.7 pts/week

Completed vs. Remaining

Status	Stories	Pts
Done	US-03, US-04, US-06, US-07, US-17	13
In Progress	US-08, US-09, US-10, US-13, US-16	15
Not Started	US-12, US-14, US-15	18

Observations

1. **Strong early progress:** Carry-over stories completed quickly in Week 1 since backend logic was already done — only UI wiring remained.
 2. **Mid-sprint plateau:** Complex UI integration (suggestions, history charts, notifications) proved harder than estimated. Riverpod provider coordination slowed progress.
 3. **Divergence from ideal:** Actual line diverged around Day 7 as the team moved from simple wiring to interconnected feature work.
 4. **Carry-over to Sprint 3:** US-08, US-09, US-10, US-13, US-16 need finishing. US-12, US-14, US-15 not started.
 5. **Root cause:** Underestimated complexity of connecting state providers across features and time needed for integration testing.
-

Sprint 2 progress as of sprint end. Work continues.
